

# Le Sueur County Justice Center



## Weekly Update

**Week of 3/11/2019 - 3/15/2019**

Spring is near! This week was another busy one. Carpet installation has started in the lower and first levels. This is following acoustical ceiling tile and fixture installs. More storefront was added in the main lobby, as well as counter tops! The jail still progressed with painting the day rooms, detention glass installation in the frames and doors and ceiling grid! Up on second, interior stone continued around the elevator shaft and accent walls. One of the courtroom platforms was completed, with the second one close behind. Painting activities and light fixtures continued upstairs as well as all second floor restrooms were tiled and grouted this week!

Next week finishes will continue throughout the project. This includes carpeting, wall base, painting, and ceiling grid/pad installation. More detention glass will be installed and will start detention hardware in the jail as well as security wiring and cabling! Wood ceilings start boarders and grid on first floor lobby, and all interior stone will be completed!

Miscellaneous finishes will begin throughout the project such as main lobby display cases, marker boards, light fixtures, plumbing fixtures and lockers in the work release area!

Have a wonderful weekend and upcoming week!



## Next Week's Events

Carpet and Ceiling Pads will continue in areas of first floor!

Ceiling grid and painting continues on second floor!

Courtroom activities continues with electrical rough in, and jury/judge platforms!

Exterior windows and frames will continue on the west side of the building

Decorative wood ceilings to being on the main level!

The last majority of the Interior stone will be completed!

Detention doors finishes and hardware will begin in the Jail!

**ADOLFSON  
& PETERSON  
CONSTRUCTION**  
435 East Derrynane St.  
Le Center, MM, 56057  
[www.a-p.com](http://www.a-p.com)




The last wall of interior stone on the second floor began with detailing the corners and base!



The last few panels of interior storefront at the main lobby were installed with glass! Making way for the finishes in this area!



Counter-tops were installed throughout first floor! This include break rooms with plumbing fixtures and the main lobby desk with deal tray accessories!

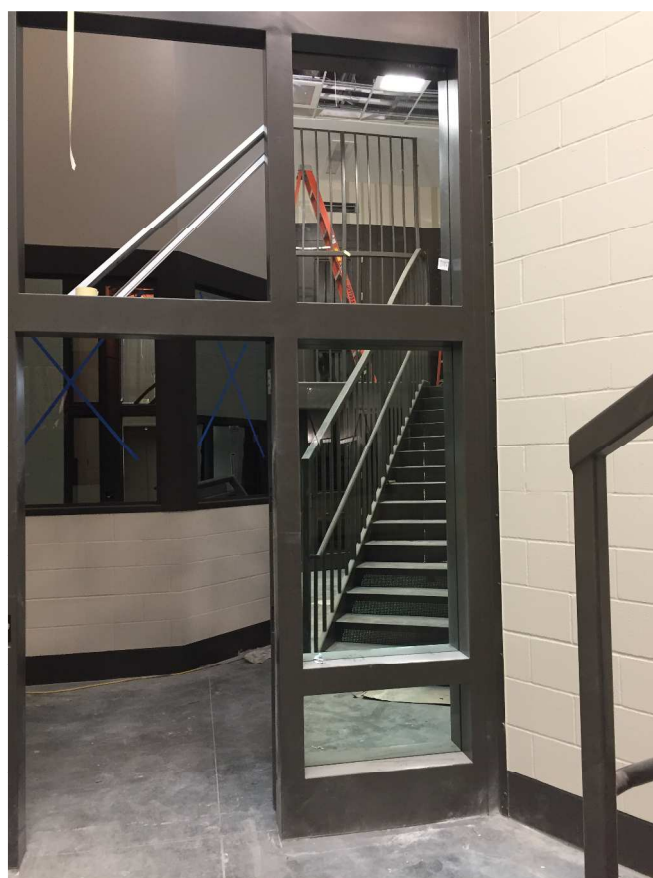

Detention glass was set this week in the day room and master control frames. This type of glass has a mirror effect in order to not see through it well

