

Le Sueur County Justice Center



Weekly Update

Week of 9/24/18 - 9/28/18

Happy Friday Everyone!

Fall is officially here. This week was yet another busy week. MEP (Mechanical, Electrical and Plumbing) and sprinkler rough ins continued in every area of the project, with the focus on the jail space and starting in the recently poured sally port and garage. Masonry walls continued to go up in the jail along with detention frame installs. This is to get ready for the prefabricated cell delivery in the upcoming week. Framing and drywall activities continued on the second level nearing its completion and making way final rough ins and drywall. On the lower level, the last masonry wall was built. Towards the end of the week the remaining rooftop mechanical units were installed via crane. The biggest one (pictured above) weighed 13,600 pounds!

Next week the site will focus on preparing for winter. This includes covering up openings with poly., building temporary doors for access, as well as getting everything ready for the installation of the final two precast panels to officially seal the building. Also, site work will begin Monday with grading the parking lot, surveying the locations of the concrete curbs and light poles and the start of electrical work, irrigation and miscellaneous items. Work in the jail will still be the main focus for MEP trades with rough ins, and insulations, and masonry walls will continue being built along side the installation of detention frames. Capping of the final roof installation on the main entrance canopy!

Have a wonderful and safe weekend!



Next Week's Events

-MEP Roughins continue through the site

-Site work will begin! This includes earthwork, surveying, and the start of working on electrical, light pole bases, irrigation, concrete curb and grading throughout the site

-Final roofing installation on the canopy, marking the roof be 100% complete!

- Masonry walls through out the jail area


-Layout of the prefabricated cells

-Framing and sheet rocking soffits, ceiling walls and other areas of the second level!

ADOLFSON
& PETERSON
CONSTRUCTION
435 East Derrynane St.
Le Center, MM, 56057
www.a-p.com



The final windows were installed on the upper roof since the brickwork install and washing was completed!

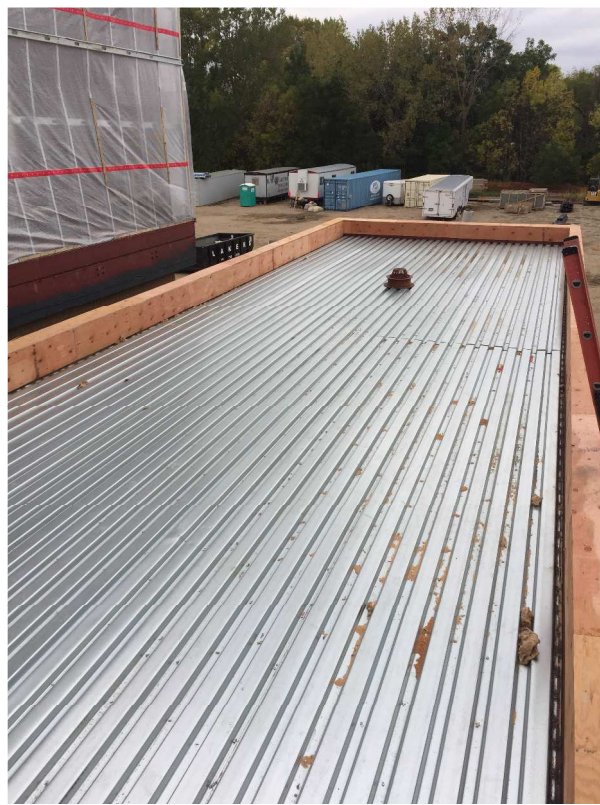

Steel decking, roof drain and wood blocking was installed this week getting ready for the last area of roofing material!



MEP rough in continue through the Jail area of the building with ductwork, plumbing piping getting installed and insulated and electrical conduits all ready for the cells



Masonry walls continue to be built up in the jail area along with the setting and installation of detention door frames!
