

Le Sueur County Justice Center



Weekly Update

10/15/18-10/19/18

Another exciting week on site! Rough ins continued on lower level, first floor offices and jail and all of second floor. Lower level made progress with sheetrocking and insulation. Hollow metal and detention door frames were installed through the first floor and started on second floor openings. Jail work included more masonry walls of the day rooms, metal framing and rough in above the installed cells and fire stopping! The main stairwell treads were poured and is the main access to the other levels. The south stairwell started installation late this week. The biggest effort was the site work this week because of the wonderful weather. Grading the parking lot lead way to the placement of concrete curb and gutter with a curb machine (pictured above), the trash enclosure walls took off and the remaining roof top mechanical units were installed!

Next week, rough ins, sheetrock and framing, masonry walls in the jail will all continue next week. Site work will include finishing the trash enclosure, more concrete curb and gutter, paving portions of the parking and preparation for the first course of asphalt that will be placed at the end of next week. Steel work next week will focus on the first steel mezzanine in the jail pods will begin as well as finishing the south stair. Thank you and have a wonderful weekend!



Next Week's Events

-Mechanical, Electrical and Plumbing Rough ins continue throughout the building!

-Masonry walls in the jail section continue!

-Lower level sheetrock!

-Cell mezzanines start installation

-South stair tower steel installation

-Parking lot paving will be being!

-Preparation and installation of the first course of asphalt!

ADOLFSON
& PETERSON
CONSTRUCTION
435 East Derrynane St.
Le Center, MM, 56057
www.a-p.com




Masonry crews worked on above grade CMU walls of the trash enclosure with the nice weather at the end of the week!



Sheetrock making great progress down in the lower level. 1st and 2nd floor frames continue install!



The last mechanical roof top unit was installed this week!

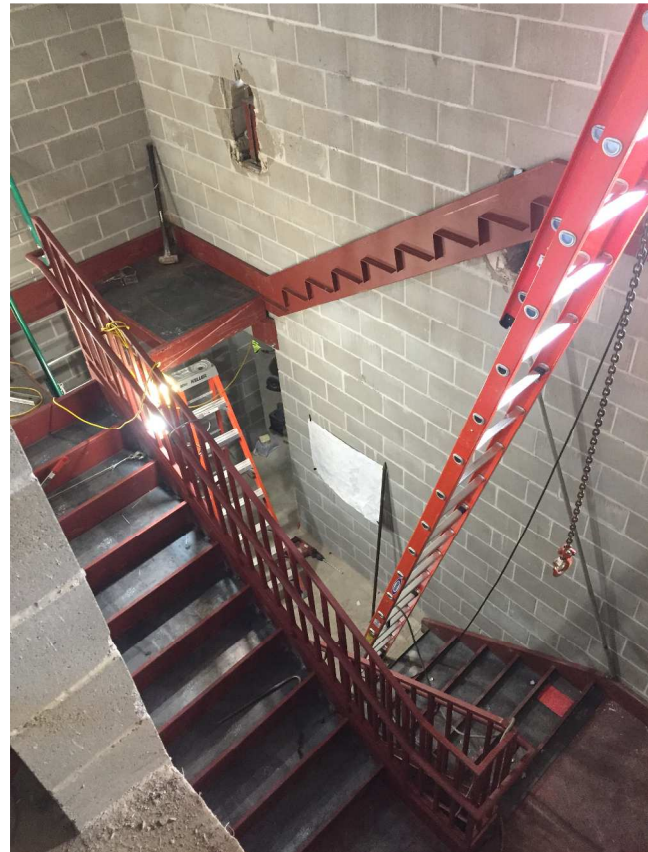

With the opening of the main stairwell, the temp scaffold stair has been removed on the south stair tower. The steel for the stairs were delivered and started install this week!
