

Le Sueur County Justice Center



Weekly Update

07/09 - 07/13

Another very eventful and productive week on the jobsite! To start the week, we poured roughly 80 yards of concrete on the west side of Area A. It was a slab on grade pour and it covered half of the area. After the concrete hardened, the HVAC crew began to hang vents from the ceiling. On the east side of Area A, the electricians and plumbers continued to bury their MEP underground piping and conduit. The framers have been working on the 2nd floor and preparing for the walls to get pinned up, while the roofers have been laying insulation and EPDM roofing on the Area C roof. They're nearly complete with the roof on that area!

Next Week's Events

Grading and prepping for another concrete pour on the east side of Area A. The pour will then follow

Roofers will continue to lay insulation and EPDM roofing on Area C, and will then move onto Area A and begin roofing activities there.


The framers will finish up on the second level and then move to the first level and begin framework.

Electricians will continue with rough-ins and Area B.

Mechanics will continue working on roof drains in Area B, while the HVAC crew continues to hang ventilation systems in Area A



HVAC workers began hanging vents from the roof this week.

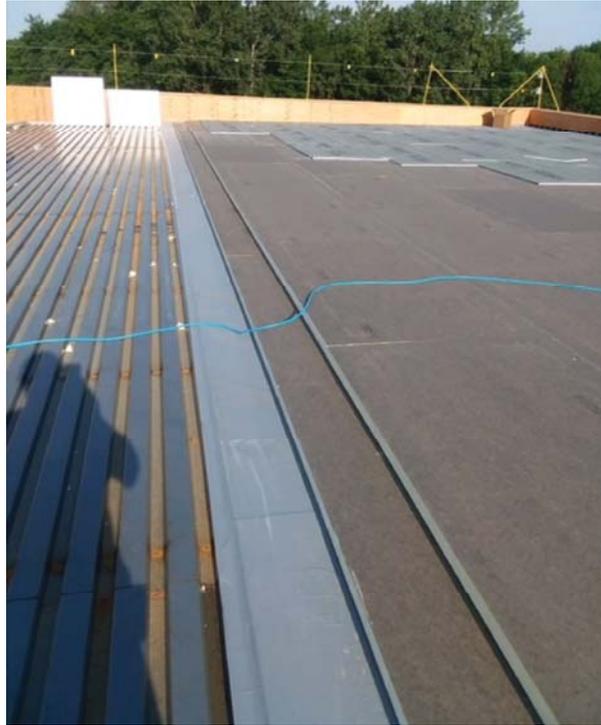

The roofers began laying insulation and EPDM on the roof. This was shot earlier in the week, they are now nearly complete with this portion of the roof!



Earthworkers dug trenches in order to place the drain tile underground on the east side of Area A. Once this is graded over on Monday, we will be ready for another pour!
