

Le Sueur County Justice Center



Weekly Update

09/03/18 - 09/07/18

Although we lost the roofers for a day at the beginning of the week due to rain, they are nearly 100% complete with the whole roof! Once they finish up Area B early next week, they will have completed the roof. On the lower roof of Area A, the masonry crew started laying their brick wall. At the main entrance, the framers sheetrocked the whole entryway and will apply the air barrier to it next week. In area B, the skylight frames were prepped and set in the roof so next week we will have the skylights installed. Throughout area A, on the main and second level, MEP rough ins continue to make progress. In the LEC garage, equipment operators were grading dirt in order to prep that area for a pour that is going to happen next week. Also, the trench drains in the LEC garage got concrete pours and they are now set in place.

Have a great weekend everybody!



Next Week's Events

The roofers will finish up on Area B! This will complete the whole roof of the building

The masonry crew will continue laying brick on the lower roof of Area A

MEP rough-ins will continue progressing throughout the building

Skylights will be set in the Area B Dayrooms


The LEC Garage floor will be poured with concrete

The framers will continue framing and sheetrocking walls throughout the building

ADOLFSON
& PETERSON
CONSTRUCTION
435 East Derrynane St.
Le Center, MM, 56057
www.a-p.com



Metal wall panels were set on the wall on the upper roof of Area A!

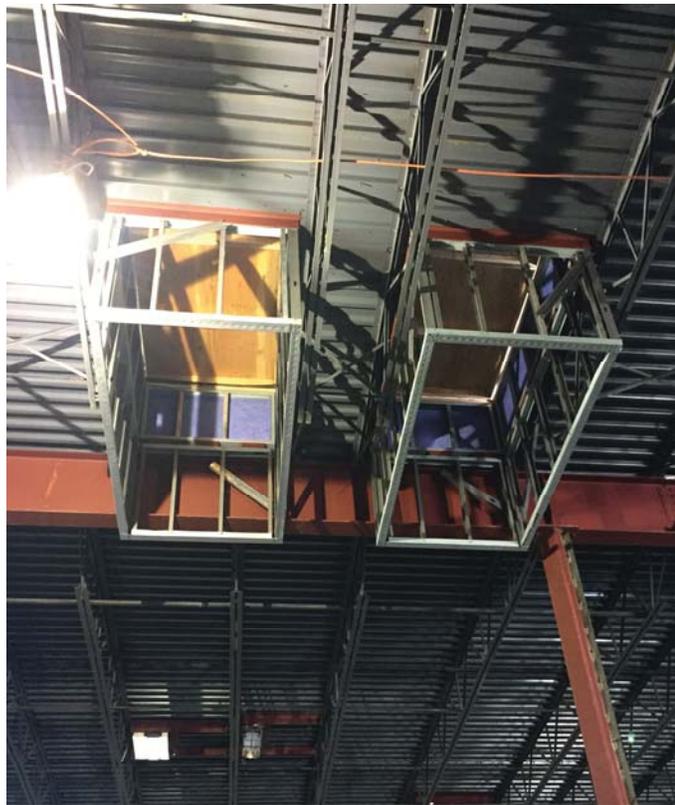

Skylight frames have been made, so now the skylights are ready to be set!



The roofers continued to lay EPDM roofing on Area B. They will be completely done early next week!



More structural CMU walls were put up in area's A & B
